\$5.00 fee for permit

ISLAND COUNTY HEALTH DEPARTMENT Postoffice Box 218, Coupeville, Washington


Phone ORange 8-4008

CATION FOR PERMIT TO CONSTRUCT A SEWAGE DISPOSAL SYSTEM,
APPOCATION FOR PERMIT TO CONSTRUCT A SEWAGE DISPOSAL SYSTEM. AND FORM'S NAME: F.J. Y & T. G. TOSS
Mailting address: R. I LANGLEY, WASh. 98260Phone:
Maijung address: F. J. LANGLEY, WASh. 98260Phone: Logary Dn Office Mastruction site: UELLTH DEPARTMENT ruction site:
UELLIN "
Street number Distance to nearest cross road Legal description: Lot/ Sec. 4 Twp. 29/Blk. Rge 3 Addition 30-4-29
Type of use home No. of bedrooms Z No. of bathrooms /
Lot width: 408 ft. Lot depth: 237 ft. 41, 196 sq. ft.
Source of drinking water: Public supply Private Well
Dig a hole at least 4 feet deep in the disposal field area. After the hole is dug record the soil conditions at the following depths: (record as sand, gravel, clay, packed sand, loam, etc.)
12 inches Sand 24 inches Sand 36 inches Sand 48 inches Sand
2. Furnish sketch on reverse side hereof, or attach plot plan of premises showing - a. Distances between property lines and sewage system. b. Distance to any well, spring, creek or other body of water. c. Show direction and approximate slope of lot. d. Show the location and layout of the septic tank system. e. List size of septic tank, inside length, inside width, water depth capacity in gallons. f. Width, length and depth of drain lines, amount of gravel under tile, amount of gravel over tile, type of tile used. g. Location of buildings and driveways, swimming pools, etc.
Percolation test made Date ff 1 Result: 1" in 3 min
I hereby state that the information above and on the reverse side here of, or attached hereto is correct and true to the best of my knowledge. I understand that the permit must be otained before any construction is begun, either on the building or the sewage disposal system, and a satisfactory inspection of system is required before the sewage disposal system may be backfilled, or put to use. Signed: Date: 1//61
Signed: Date:
Contractor
Plan approved: <u>Oxid</u> Permit No. 15-7 Receipt No. 1908 Date 7/5/67 Final inspection approved Rejected By: Oxide Date 1-19-68
Remarks: Fuld was . T Code
Remarks: Filly maple T. O.
Remarks: Folymorect. (00)
_guo'

Inside 7 Inside 48 Water 4 Gallons 150

Field Total
Drain: Length 75 Width 2 Depth 30 No. of lines 2

Gravel: Size: 12 Overtile 2 inches, Undertile 6 Inches.

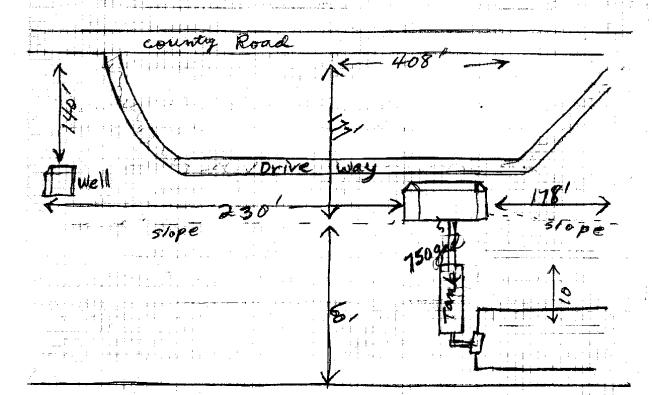

1
