

CL
F

HALL COUNTY BOARD OF HEALTH
P.O. BOX 1295, 430 PRIOR STREET GAINESVILLE, GA 30503
APPLICATION FOR CONSTRUCTION PERMIT AND INSPECTION
FORM FOR ON-SITE SEWAGE MANAGEMENT SYSTEM

Application Date: Mar 16, 2004

Permit Number: S-069-2004-00457

Property Address: 3518 LAKE BREEZE LANE
GAINESVILLE, GA 30506

Lot Number: 42

Subdivision: HARBOUR POINT - PHASE 2

Builder/Company: LEE WAGNER

Owner's Name: TOM BURG

Owner's Address: 7565 KINSELLA COURT
DUNWOODY, GA 30118

Phone: 7

Fax:

Facility Type: RESIDENCE

Lot Size:

Bedrooms: 3 CH

Percolation Rate: 30-45 kph

Absorption Field Area:

Linear Ft:

Square Ft:

Trench Width:

Trench Depth:

100' x 4

30 Inches

24"-30"

Water Supply: PUBLIC

Garbage Disposal: Yes

Grease Trap: Gals.

Water Table: 72

Plumbing Level: BASEMENT

Type System: EZ FLOW 1203T

Field Layout: SERIAL DISTRIBUTION

Soil Type: RION

Septic Tanks:

1500 Gals.

Dosing Tank:

Gals.

Directions:

MUST INSTALL SEPTIC SYSTEM AFTER FOUNDATION AND PRIOR TO CONSTRUCTION. DUE TO EXTREME SLOPES MAY REQUIRE AREAS FOR SEPTIC SYSTEMS TO BE BENCHED. Do not cut or fill in primary or recovery system areas.

Disclaimers:

REPORT ALL BURIED TRASH/DEBRIS/MULCH TO ENVIRONMENTAL HEALTH

DIVERT ALL WATER AROUND SYSTEM

INSTALLER MUST HAVE CERTIFICATION CARD ON SITE

IF INSTALLER FINDS UNSUITABLE SOIL OR OTHER PROBLEMS, STOP WORK & CALL ENVIRONMENTAL HEALTH IMMEDIATELY

INLET & OUTLET TEES MUST BE INSTALLED & SECURE FOR INSPECTION

ALL SYSTEMS MUST ACCOMMODATE THE NUMBER OF BEDROOMS

MUST PAY NEW PERMIT FEE IF REPAIR OR ADDITION WILL NOT USE ANY PART OF EXISTING SYSTEM

IF WITHIN 10 FEET OF DRAIN LINE, ALL WATER SUPPLY LINES MUST BE ENCASED IN A SINGLE LENGTH OF PIPE AND 12" ABOVE THE TOP OF THE DRAIN LINE

SEDIMENT AND SOIL EROSION CONTROLS MUST BE SUFFICIENT AND REMAIN IN PLACE

Issuance of a construction permit for an on-site sewage management system and subsequent approval of same by representatives of the Georgia Department of Human Resources or County Board of Health shall not be construed as a guarantee that such systems will function satisfactorily for a given period of time, furthermore, said representatives do not by any action in effecting compliance with these rules, assume any liability for damages which are caused, or which may be caused, by the malfunction of such system.

I hereby apply for a construction permit to install an on-site sewage management system and agree that the system will be installed to conform to the requirements of the rules of the Georgia Department of Human Resources, Chapter 290-5-25. I have read and will comply with the additional requirements printed above. I understand that final inspection is required and will notify the County Health Department upon completion of construction and before applying final cover

Signature(Owner or Applicant)

ONLY VALID FOR CONSTRUCTION IF SIGNED
PROPOSED DRAWING IS ATTACHED

5-12-04

KH

Rochester 1500 gal plastic

Label Filter


EZ Flow ROST- 150' total

Avg TD: 30"-36"

STD: $\leq 12"$

Repair

SKETCH IS APPROXIMATE
NOT TO SCALE

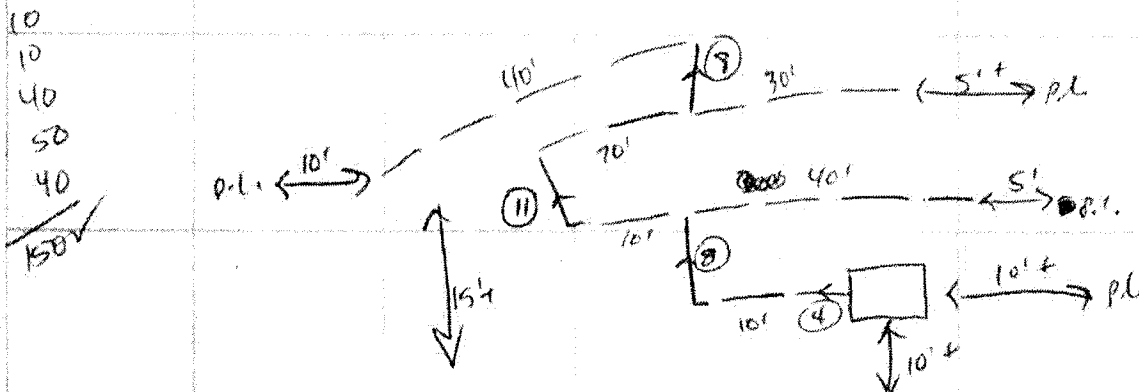

Proposed
House

Lake Breeze Lane
